PCC AIRFOILS-2 WEEK LOOK AHEAD
COMPLETION DATE JUNE 1 2008

ID	Task Name	Duration	Start	Finish
1	**PLANT AREA**	10 days	Mon 5/5/08	Fri 5/16/08
2	PROCESS PLUMBING	19 days	Mon 5/5/08	Thu 5/29/08
3	WALL FINISHES	6 days	Mon 5/5/08	Mon 5/12/08
4	ELECTRICAL	10 days	Mon 5/5/08	Fri 5/16/08
5	DOOR PAINTING	3 days	Mon 5/5/08	Wed 5/7/08
6	DRYWALL FINISH	3 days	Mon 5/5/08	Wed 5/7/08
7	PERMANENT POWER	1 day	Mon 5/5/08	Mon 5/5/08
8	PAINTING	9 days	Mon 5/5/08	Thu 5/15/08
9	TUBEHEATER INSTALL	4 days	Mon 5/5/08	Thu 5/8/08
10	GAS PIPING	3 days	Mon 5/5/08	Wed 5/7/08
11	HVAC/DUCTING	5 days	Mon 5/5/08	Fri 5/9/08
12	BUILDING SECURED	1 day	Mon 5/5/08	Mon 5/5/08
13	INSTALL MANDOORS/HARDW	4 days	Wed 5/7/08	Mon 5/12/08
14	COOLING TOWER FITUP	11 days	Thu 5/8/08	Thu 5/22/08
15	OVERHEAD DOORS	8 days	Fri 5/16/08	Tue 5/27/08
16	**OFFICE**	10 days	Mon 5/5/08	Fri 5/16/08
17	PRIMER PAINTING	3 days	Mon 5/5/08	Wed 5/7/08
18	ELEC TRIMOUT	11 days	Mon 5/5/08	Mon 5/19/08
19	REMOVE WEATHER PROTEC	2 days	Mon 5/5/08	Tue 5/6/08
20	VESTIBULE/INFLOOR HEAT C	2 days	Mon 5/5/08	Tue 5/6/08
21	HVAC/RUNOUTS/GRILLS	5 days	Mon 5/5/08	Fri 5/9/08
22	LAYIN FIXTURES	4 days	Mon 5/5/08	Thu 5/8/08
23	SPRINKLER HEADS	5 days	Mon 5/5/08	Fri 5/9/08
24	CERAMIC TILE COMPLETE	4 days	Tue 5/6/08	Fri 5/9/08
25	CABS /TOPS	7 days	Tue 5/6/08	Wed 5/14/08
26	CEILING GRID	3 days	Tue 5/6/08	Thu 5/8/08
27	STAIRS/PAINT/RAILING	4 days	Thu 5/8/08	Tue 5/13/08
28	PLUMBING FIXTURES	12 days	Thu 5/8/08	Fri 5/23/08
29	FINAL CEILING INSPECTION	1 day	Fri 5/9/08	Fri 5/9/08
30	INTERIOR GLAZING	5 days	Mon 5/12/08	Fri 5/16/08
31	CONCRETE SEALING	5 days	Mon 5/12/08	Fri 5/16/08
32	CEILING PADOUT	4 days	Wed 5/14/08	Mon 5/19/08
33	DIAL TONE	1 day	Wed 5/14/08	Wed 5/14/08
34	ALARM WIRING	6 days	Thu 5/15/08	Thu 5/22/08
35	DATA WIRING	6 days	Thu 5/15/08	Thu 5/22/08
36	WALL FINISHES	5 days	Fri 5/16/08	Thu 5/22/08
37	MANDOORS	5 days	Mon 5/19/08	Fri 5/23/08
38	OFFICE FLOORING	5 days	Mon 5/19/08	Fri 5/23/08
39	LIFE SAFETY TEST	1 day	Fri 5/23/08	Fri 5/23/08
40	HVAC/PLUMBING/ELEC FINAI	1 day	Fri 5/23/08	Fri 5/23/08
41				
42				
43	**EXTERIOR**	10 days	Mon 5/5/08	Fri 5/16/08
44	PAINT BUILDING	2 days	Mon 5/5/08	Tue 5/6/08
45	ASPHALTPREP	3 days	Mon 5/5/08	Wed 5/7/08
46	RESPREAD TOPSOIL	5 days	Mon 5/5/08	Fri 5/9/08
47	PERMANENT POWER	1 day	Mon 5/5/08	Mon 5/5/08
48	FENCING/GUARDRAIL/GATES	8 days	Tue 5/6/08	Thu 5/15/08
49	METAL TRIM	5 days	Tue 5/6/08	Mon 5/12/08
50	RELOCATE LIGHTPOLE	2 days	Wed 5/7/08	Thu 5/8/08
51	PAVE FIRELANE	1 day	Fri 5/9/08	Fri 5/9/08
52	SET ROOF UNITS	1 day	Mon 5/12/08	Mon 5/12/08
53	AUTOGATE INSTALL	13 days	Mon 5/12/08	Wed 5/28/08
54	LANDSCAPING	10 days	Mon 5/12/08	Fri 5/23/08
55	CONCRETE APRON	2 days	Tue 5/13/08	Wed 5/14/08
56	CONCRETE ISLAND	1 day	Tue 5/20/08	Tue 5/20/08

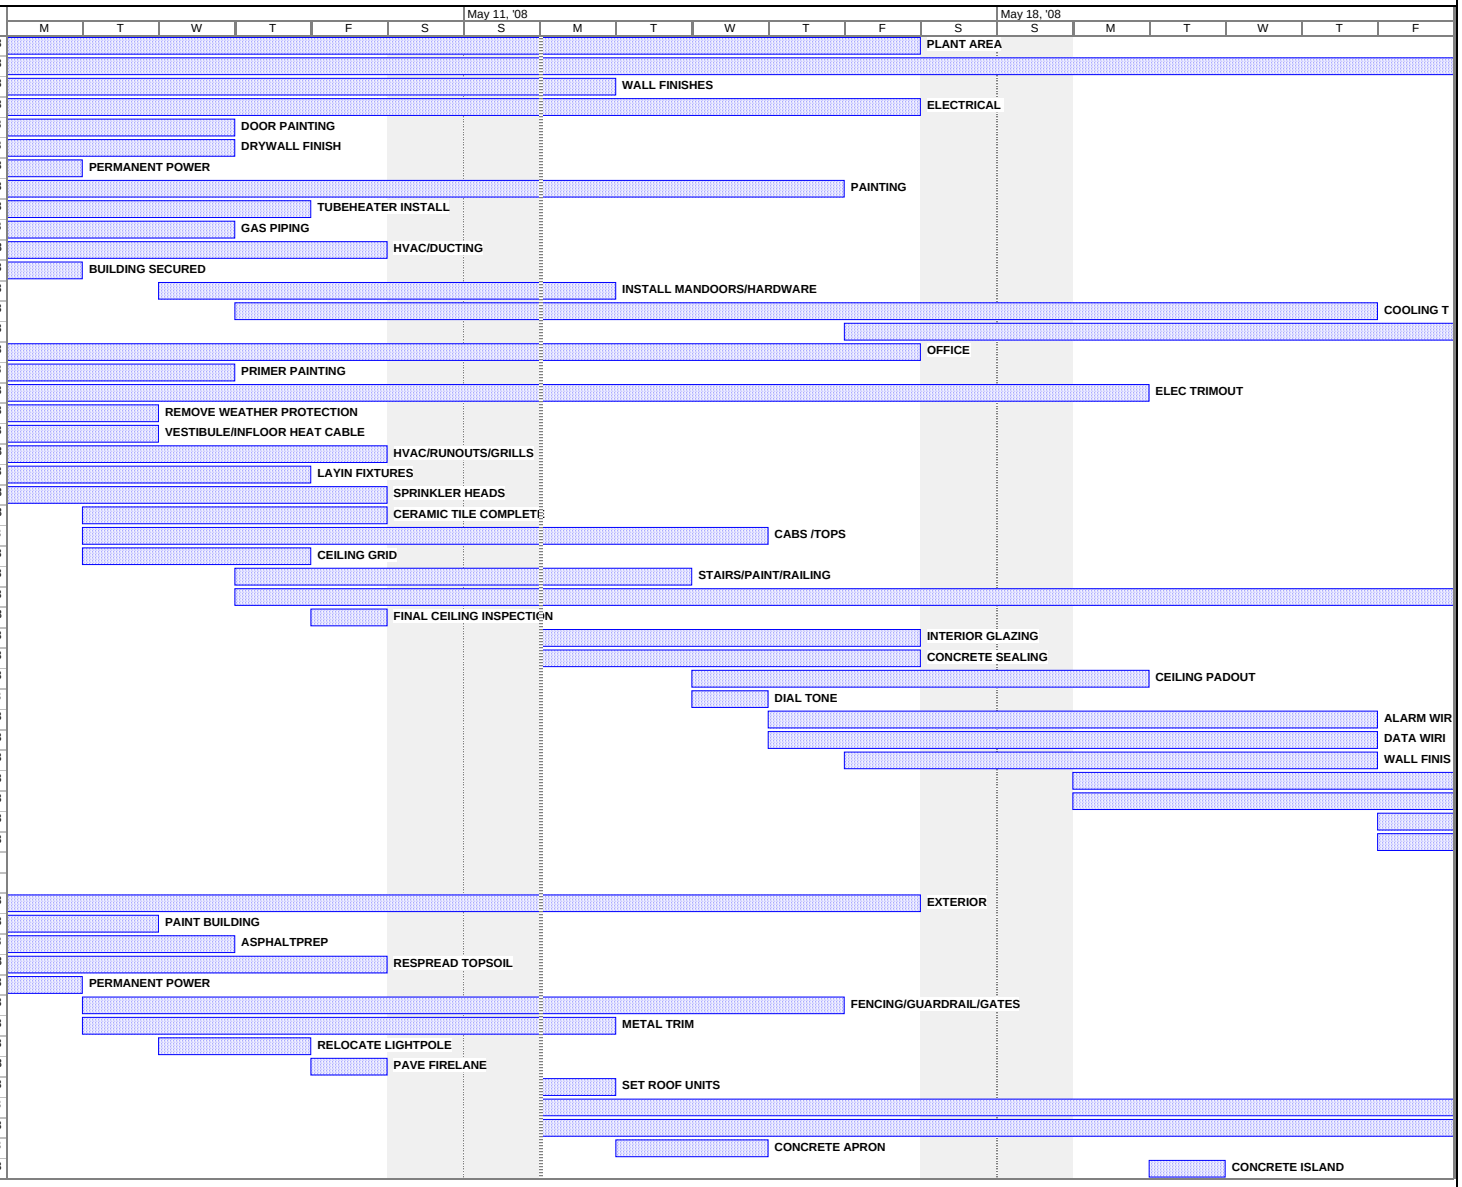

Project: 2 WEEK LOOK AHEAD 05-05
Date: Mon 5/12/08

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
